

# B4063 CYCLE IMPROVEMENT SCHEME

## ELMBRIDGE TO BRICKHAMPTON GOLF CLUB



### UPDATE BULLETIN 18.09.2023

To keep you up to date on our progress, we have outlined below the work we have completed to date, our current work areas and what you can expect in the weeks ahead.

### WORK COMPLETED TO DATE


- Phases 1A, 1B & 3A (excluding white lining) and Phases 2A (excluding MMA - cycleway coloured resin and white lining)
- Phase 4A footpath and cycleway works (excluding fire station surfacing works, MMA and white lining)
- East side of Brickhampton golf course access road (excluding MMA and white lining)
- Phase 4B, SW corner of Parton Road Junction
- Drainage works complete at Dancey Road



Phase 3A Dancey Road drainage work complete

### WORKS IN PROGRESS

- Continuing to install kerbs and footpath works in Phase 2B, west side of golf course access towards Town Cars
- Works continue in Dancey Road/ Heathdean crossroads, installing drainage and new kerbs (NE corner and NW corner)
- Kerb and bollard installation at Dancey Road
- Kerb and buffer zone installation at NW corner of Parton Road junction

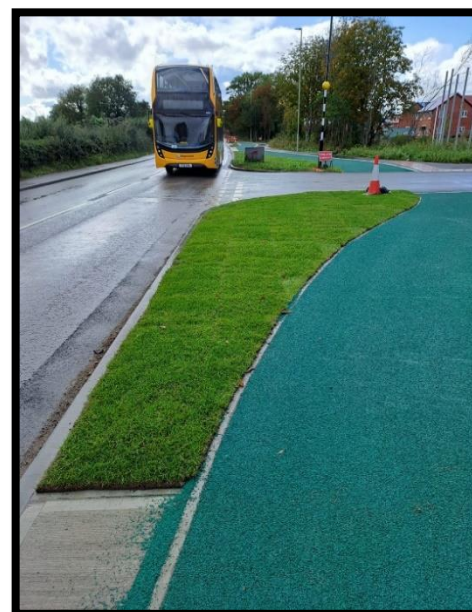

Phase 1A-3A Pirton Fields MMA cycleway resin

### UPCOMING WORKS

- White lining in Phases 1A, 1B and 3A
- Planing out existing kerbs for new carriageway kerb line at Phases 2B and 3B (Westover Court to Sandycroft Road)

### KEY TO AREAS

- 1A** North Community Fire Station to Pirton Fields
- 1B** Area opposite Tesco
- 2A** St Mary's Primary to GL3 Hub
- 2B** Westover Court to Brickhampton Golf Course

- 3A** Goldsmith Road junction to Heathdean Road
- 4A** Knights Brown compound to Fire Station
- 4B** Parton Road Junction

If you have any questions or queries please email [B4063@knightsbrown.co.uk](mailto:B4063@knightsbrown.co.uk) or call 07818 432182



# B4063 CYCLE IMPROVEMENT SCHEME

## ELMBRIDGE TO BRICKHAMPTON GOLF CLUB



### UPDATE BULLETIN 04.09.2023

To keep you up to date on our progress, we have outlined below the work we have completed to date, our current work areas and what you can expect in the weeks ahead.

### WORK COMPLETED TO DATE

- Phase 1A, 1B, 2A, 3A - excluding white lining and MMA (cycleway colour resin)
- East side of Brickhampton golf course access road - excluding white lining and MMA (cycleway colour resin)
- Cycle demarcation blocks and Tactiles installed In Phase 4A (Outside Fire station)



### WORKS IN PROGRESS

- Carriageway kerbs, road crossings and footpath works in Phase 4A in front of fire station complete, preparing formation for surfacing
- Phase 4B nearing completion, only surfacing required by road crossing
- Continuing to install kerbs and prepare formation in Phase 2B, west side of golf course access
- Works started at Dancey Road/ Heathdean Road crossroads, installing drainage and new kerbs (East)



### UPCOMING WORKS

- Continue works at Dancey Road/ Heathdean Road junction, installing new carriageway kerbs and drainage
- Preparing formation levels ready for surfacing in Phase 4A
- Trial holes at Phase 4B, on north side of road

### KEY TO AREAS

- 1A** North Community Fire Station to Pirton Fields
- 1B** Area opposite Tesco
- 2A** St Mary's Primary to GL3 Hub
- 2B** Westover Court to Brickhampton Golf Course

- 3A** Goldsmith Road junction to Heathdean Road
- 4A** Knights Brown compound to Fire Station
- 4B** Parton Road Junction

### POLITE NOTICE

It has been brought to our attention that the barriers that are in place to keep the public safely segregated from our work areas, are being moved to gain access to closed footpaths.

We must therefore highlight that it is against the law for persons to move cones, barriers, signs or temporary lights if they are not authorised or trained to do so.

